

PM

Project Procurement Management

PROJECTS

- RETENIR L'ESSENTIEL & PREPARER LA CERTIFICATION
 - ✓ QUEL EST LE CONTENU DU PROJECT PROCUREMENT MANAGEMENT ?
 - ✓ QU'EST-CE QUE LE SIPOC PROJECT PROCUREMENT MANAGEMENT ?
 - ✓ QU'EST-CE QUE LE DATA FLOW DIAGRAM PROJECT PROCUREMENT MANAGEMENT ?
 - ✓ QUELLES SONT LES NOTIONS ESSENTIELLES PROJECT PROCUREMENT MANAGEMENT ?
 - ✓ QUELS SONT LES TYPES DE QUESTIONS PROJECT PROCUREMENT MANAGEMENT ?

• PROJECT PROCUREMENT MANAGEMENT

TRENDS & EMERGING PRACTICES

- EVM – Earned Value Management
- Value Based Management
- Design to Cost
- Design to Value
- Advances Tools
- Supply Risk evaluation
- Agile & Lean approaches

PROJECT PROCUREMENT INCLUDES


- Procurement Function
- Purchasing Processes
- Industrial Organisation
- Supply Chain Management
- Contract & Legal

PROJECT PROCUREMENT PROCESSES

- Plan Procurement Management
- Conduct Procurement
- Control Procurement




• LE SIPOC PROJECT PROCUREMENT MANAGEMENT

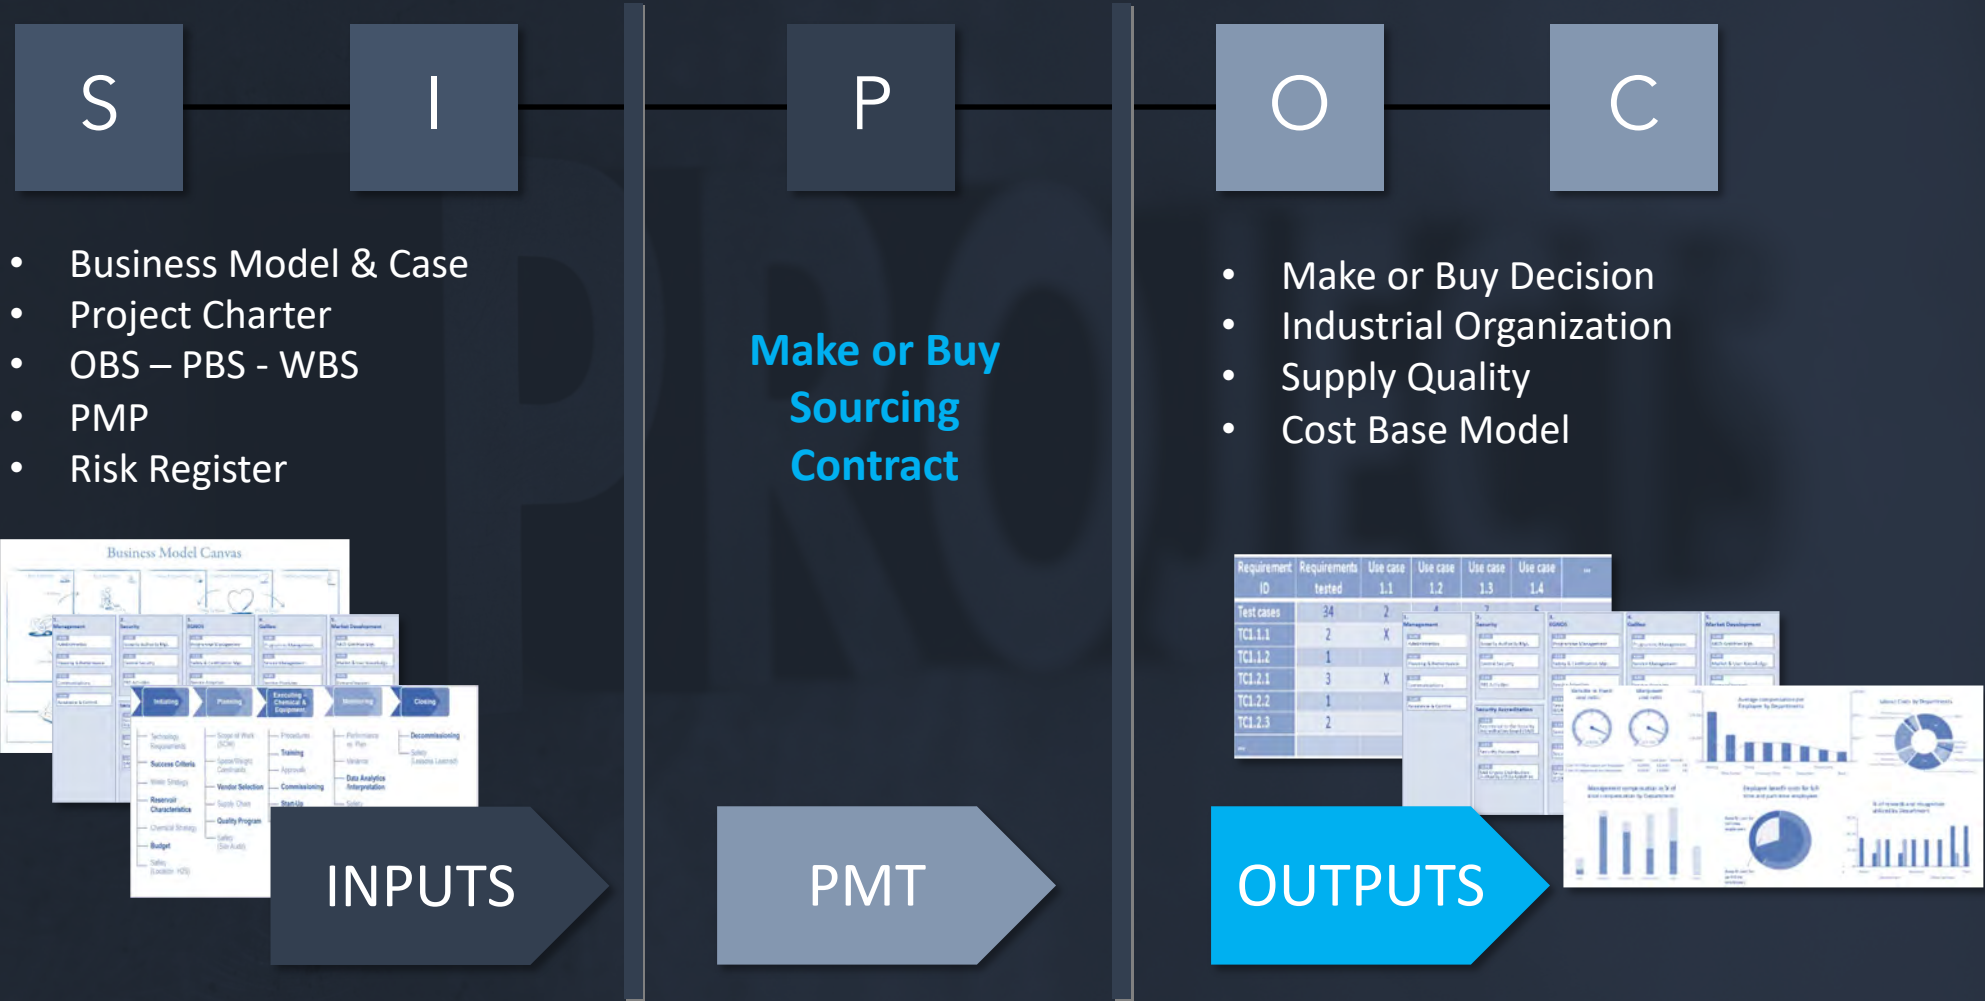


• LE DATA FLOW PROJECT PROCUREMENT MANAGEMENT

	Project Management Process Group				
	INITIATING	PLANNING	EXECUTING	MONITORING & CONTROLLING	CLOSING
Integration Management	Develop Project Charter	DEVELOP PROJECT MANAGEMENT PLAN	- Direct & Manage Project Work - Manage Project Knowledge	- Monitor & Control Project Work - Perform Integrated Change Control	Close Project or Phase
Scope Management		- Plan Scope Management - Collect Requirement - Define Scope - Create WBS		- Validate Scope - Control Scope	
Schedule Management		- Plan Schedule Management - Define Activities - Sequence Activities - Estimate Activities - Develop Schedule		Control Schedule	
Cost Management		- Plan Cost Management - Estimate Costs - Determine Budget		Control Costs	
Quality Management		Plan Quality Management	Manage Quality	Control Quality	
Resources Management		- Plan Resource Management - Estimate Activity Resources	- Acquire Resources - Develop Team - Manage Team	Control Resources	
Communication Management		Plan Communications Management	Manage Communications	Monitor Communications	
Risk Management		- Plan Risk Management - Identify Risks - Perform Qualitative Risk Analysis - Perform Quantitative Risk Analysis - Plan Risk Response	Implement Risk response	Monitor Risks	
Procurement Management		Plan Procurement Management	Conduct Procurement	Control Procurement	
Stakeholder Management	Identify Stakeholders	Plan Stakeholder Engagement	Manage Stakeholder Engagement	Monitor Stakeholder Engagement	


• LE DATA FLOW PROJECT PROCUREMENT MANAGEMENT

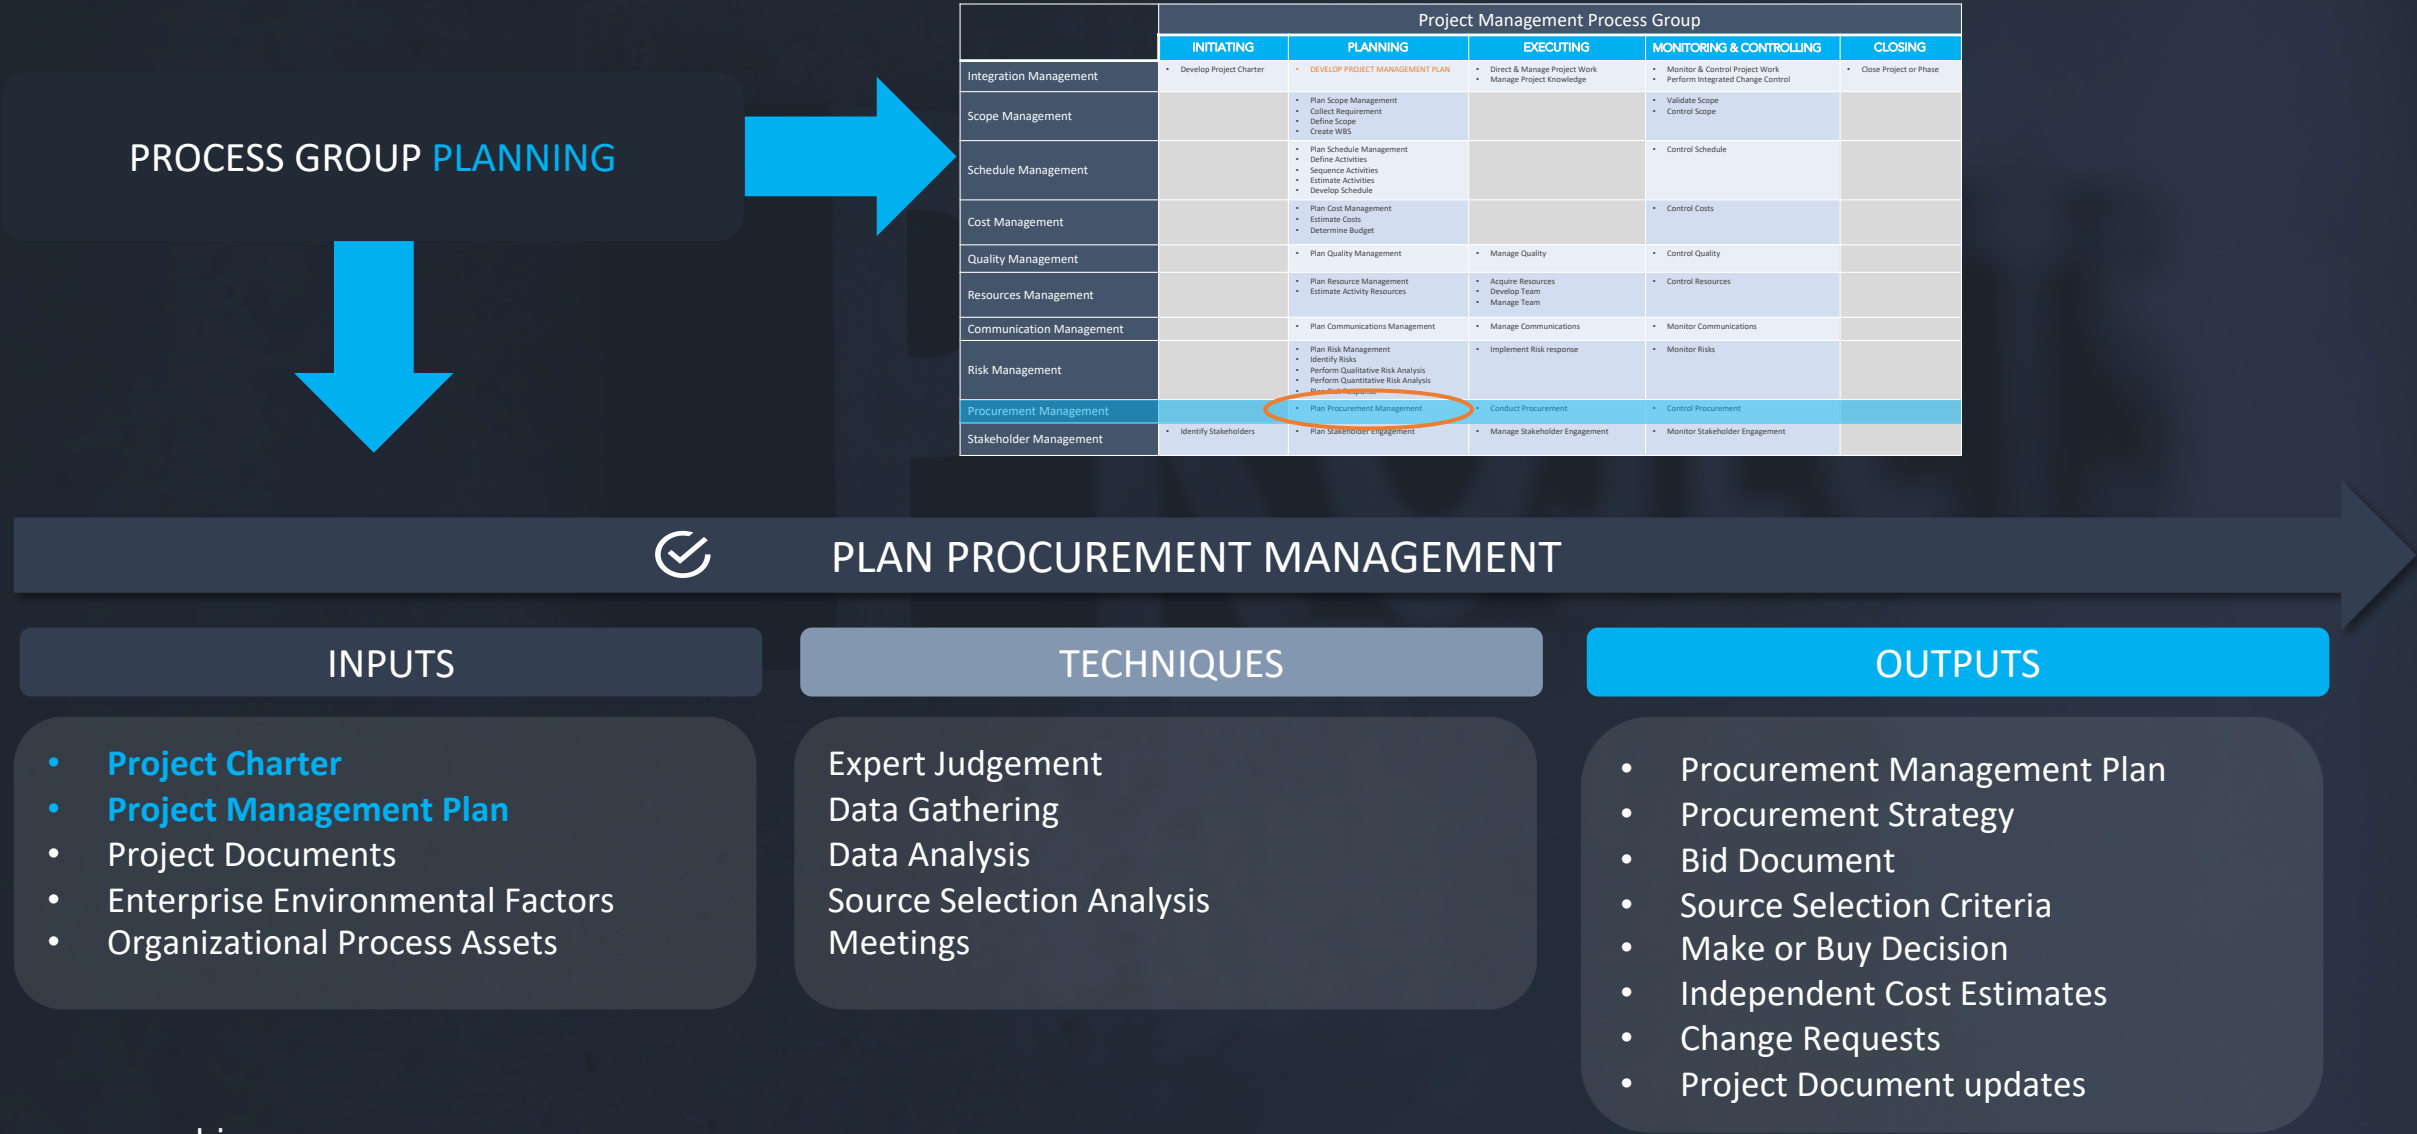


• LE DATA FLOW PROJECT PROCUREMENT MANAGEMENT

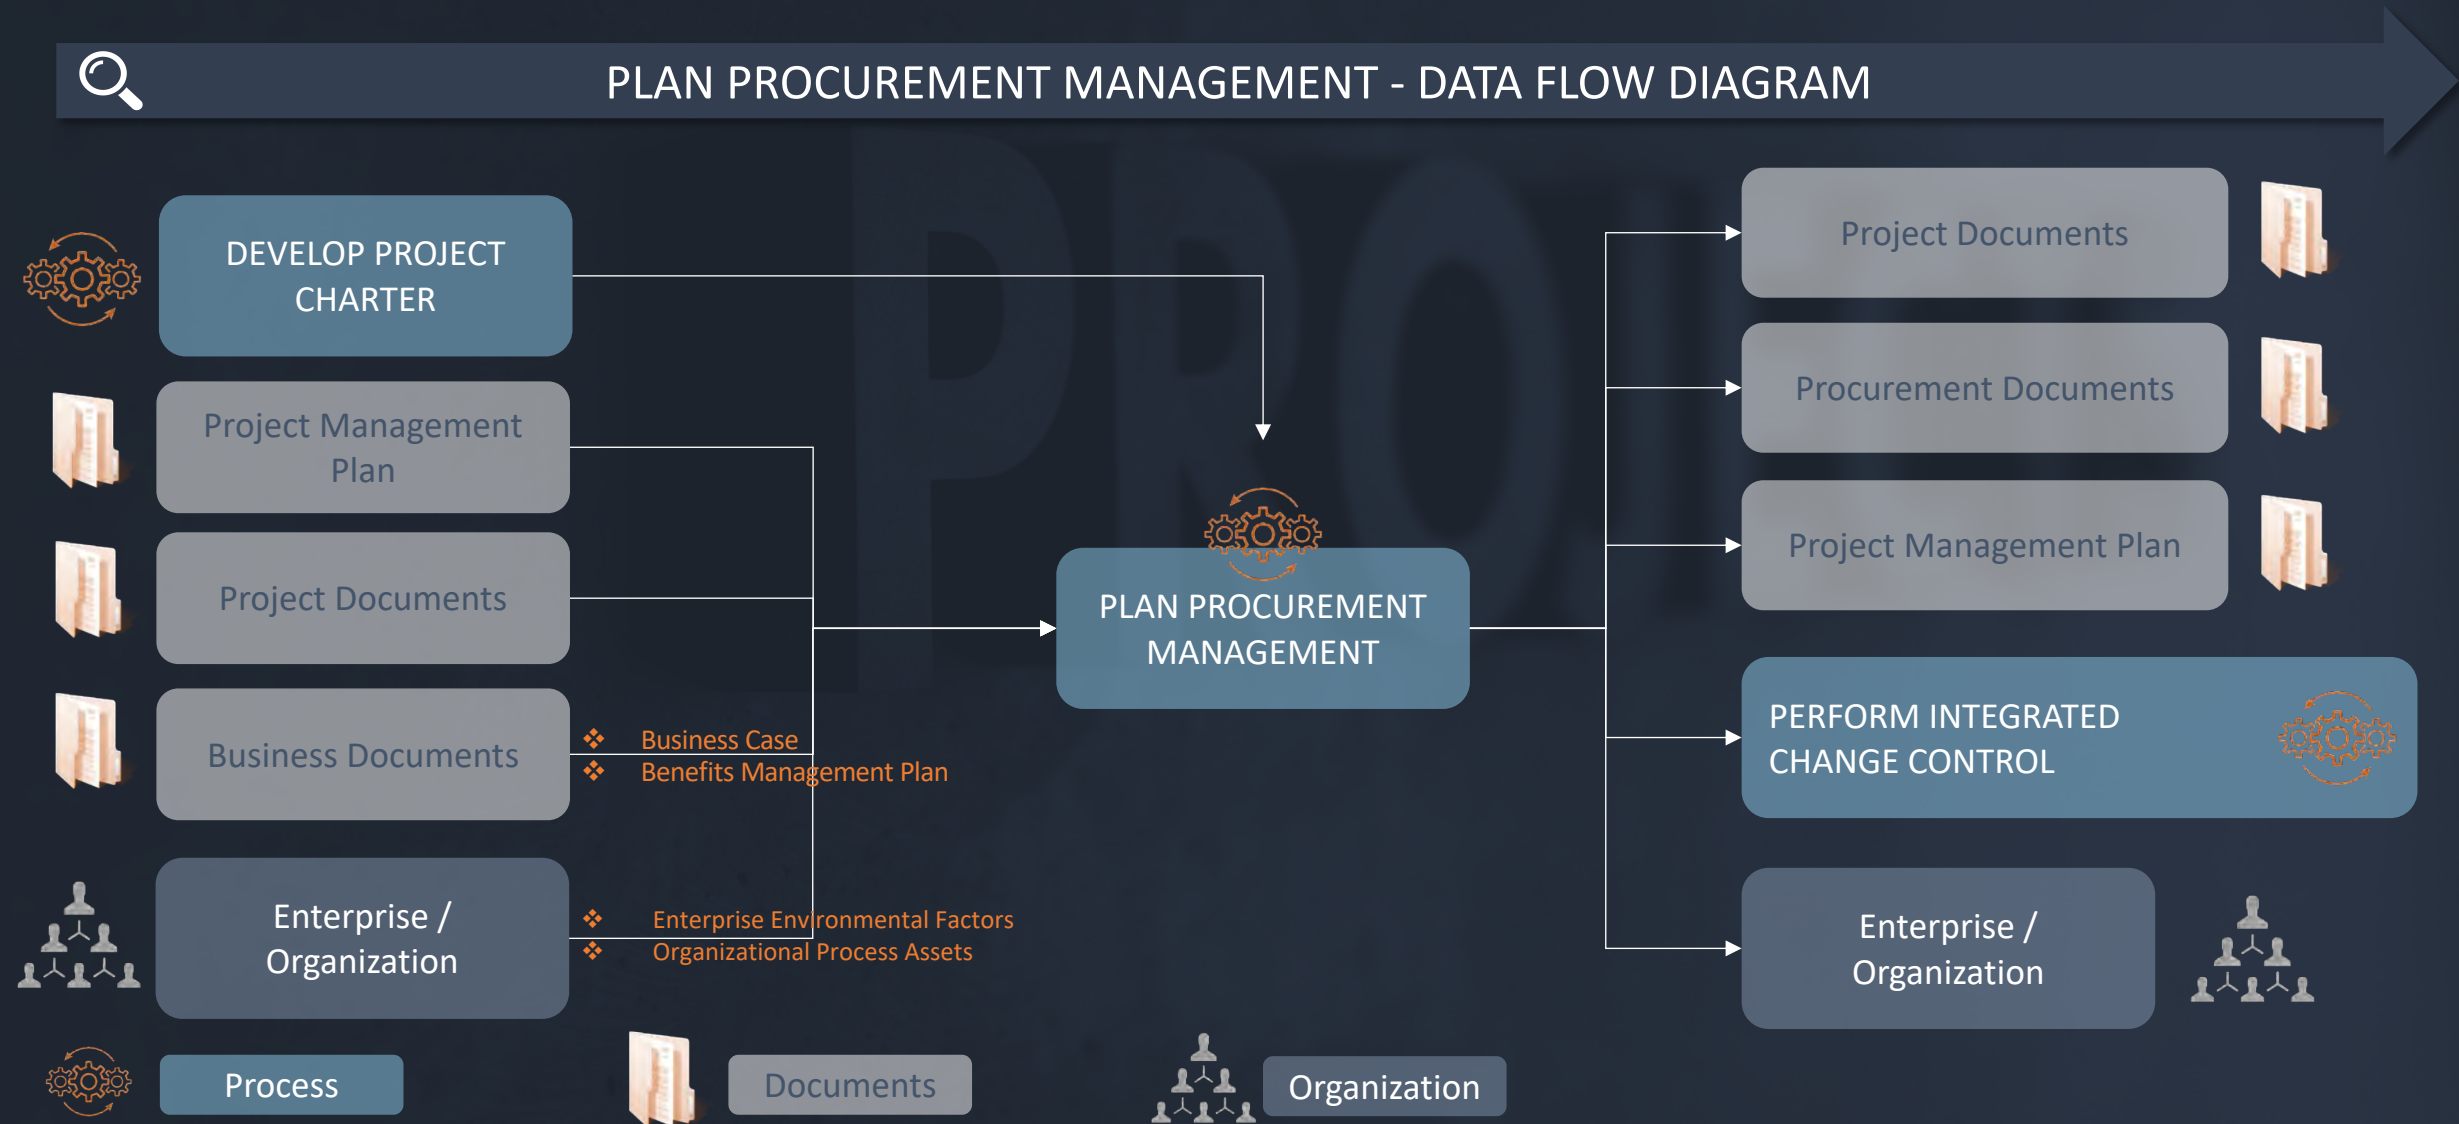

• LE DATA FLOW PROJECT PROCUREMENT MANAGEMENT

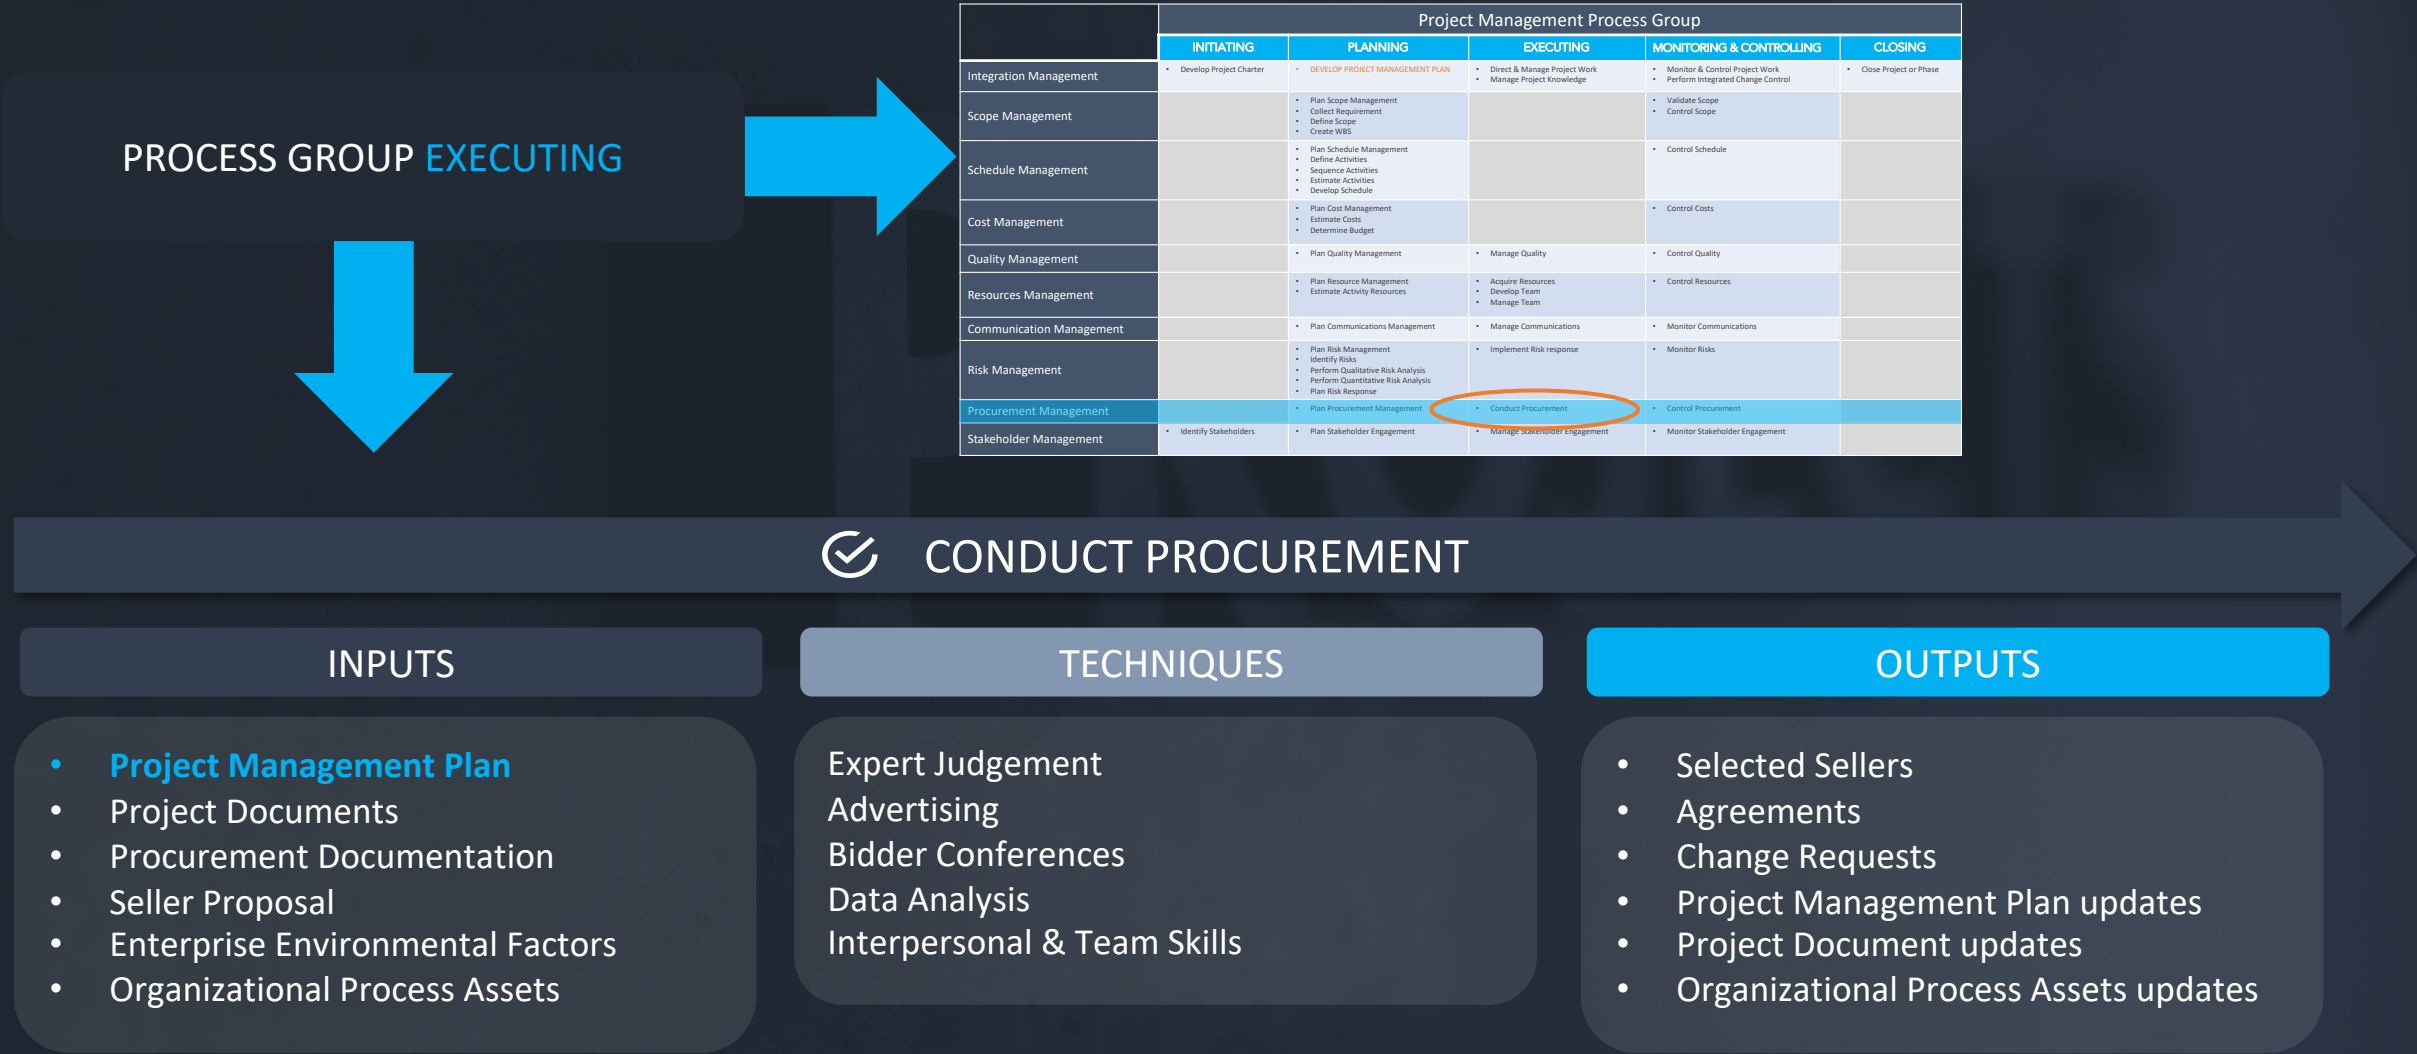

• LE DATA FLOW PROJECT PROCUREMENT MANAGEMENT

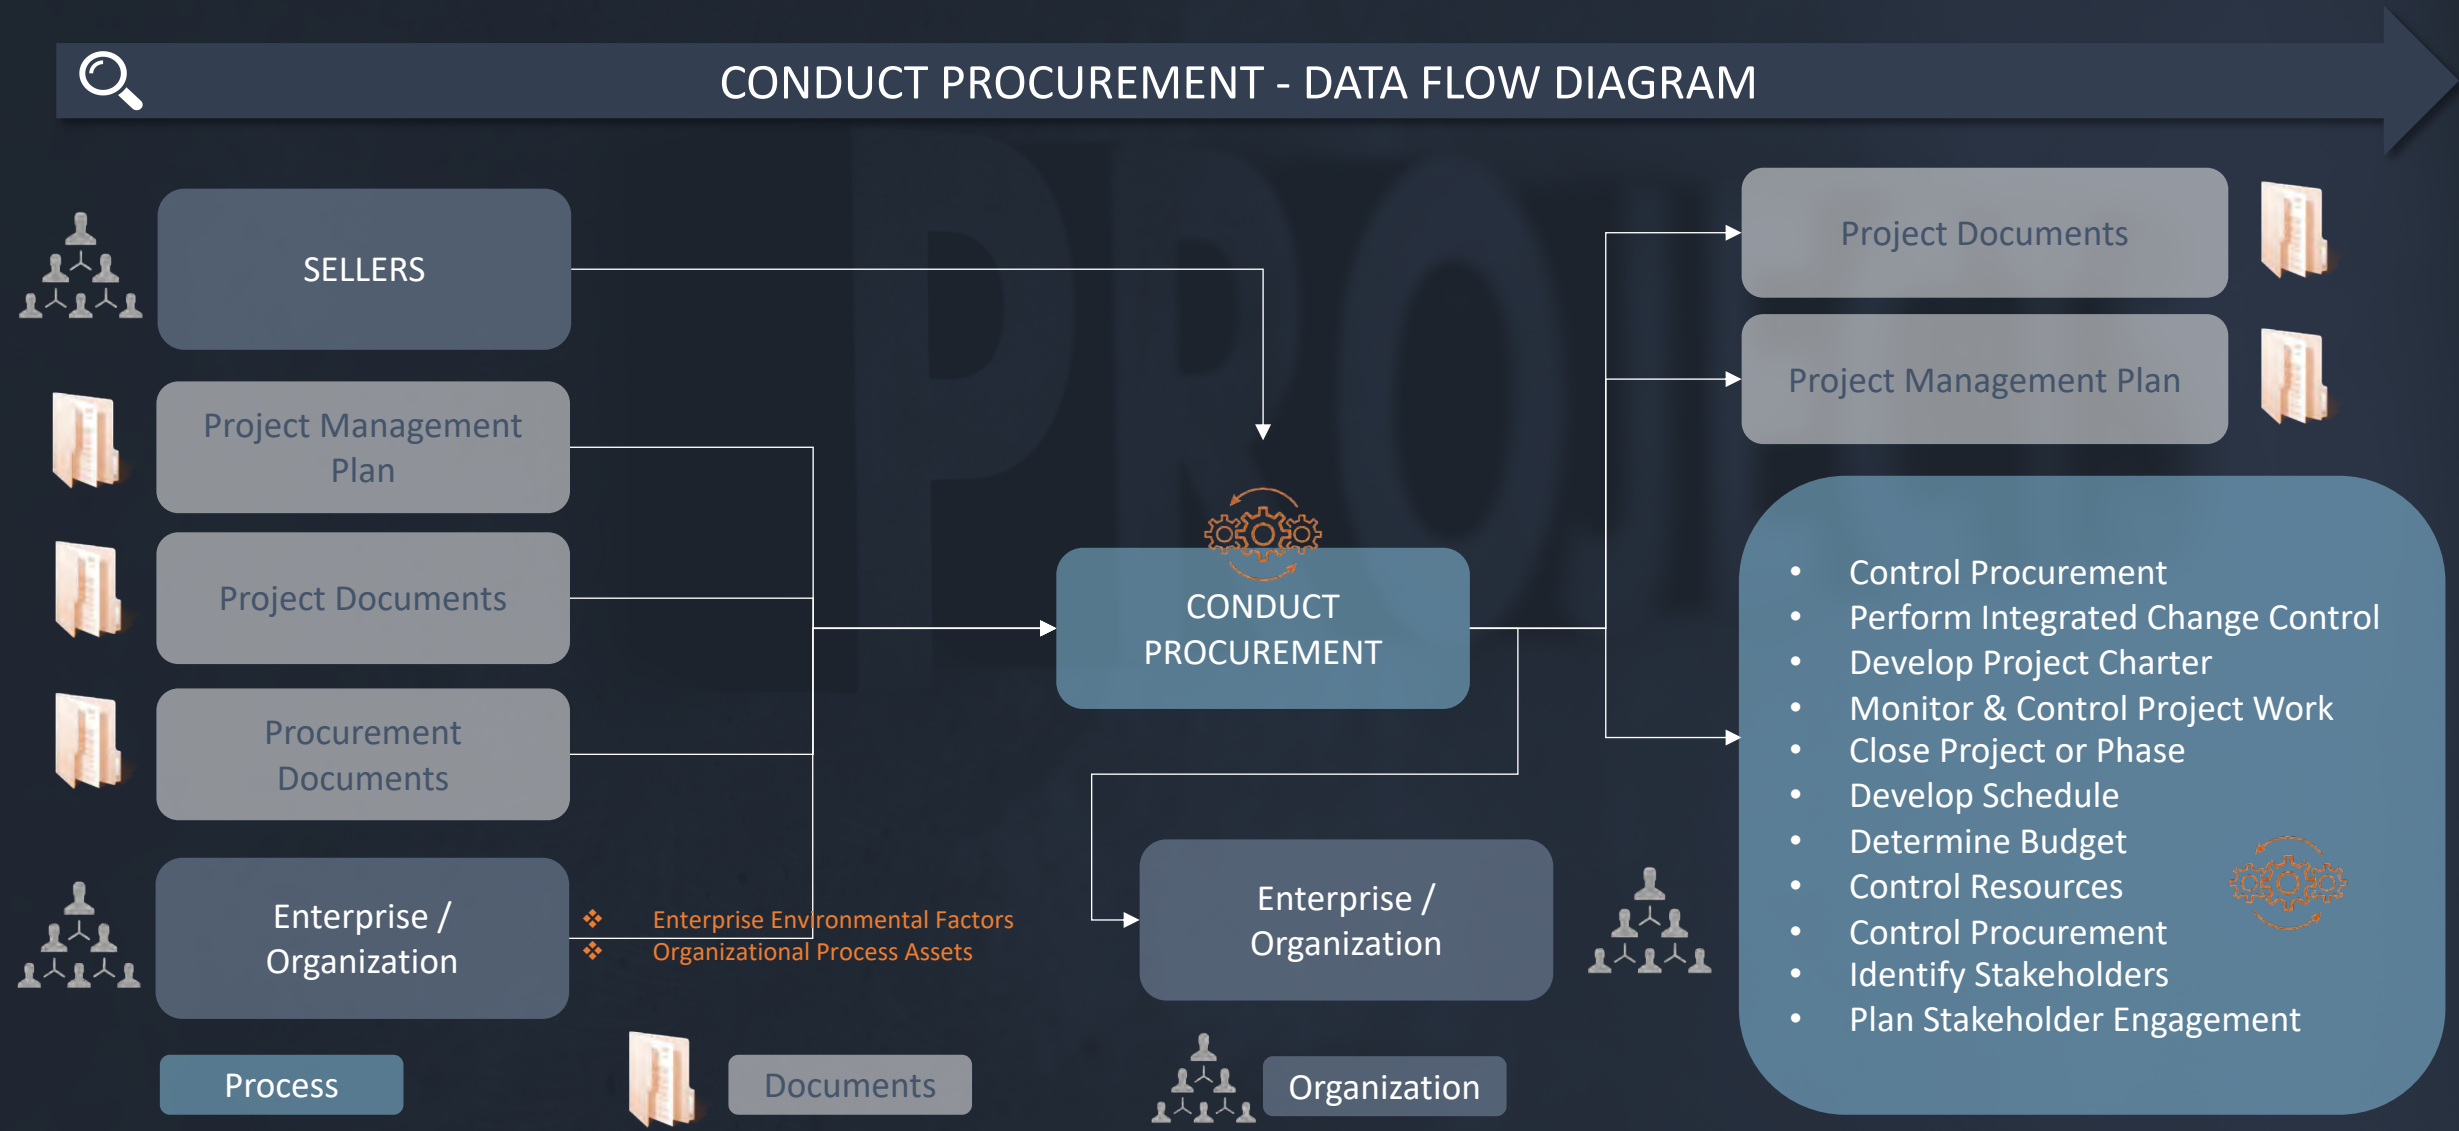

• LE DATA FLOW PROJECT PROCUREMENT MANAGEMENT



	Project Management Process Group				
	INITIATING	PLANNING	EXECUTING	MONITORING & CONTROLLING	CLOSING
Integration Management	• Develop Project Charter	• DEVELOP PROJECT MANAGEMENT PLAN	• Direct & Manage Project Work • Manage Project Knowledge	• Monitor & Control Project Work • Perform Integrated Change Control	• Close Project or Phase
Scope Management		• Plan Scope Management • Collect Requirement • Define Scope • Create WBS		• Validate Scope • Control Scope	
Schedule Management		• Plan Schedule Management • Define Activities • Sequence Activities • Estimate Activities • Develop Schedule		• Control Schedule	
Cost Management		• Plan Cost Management • Estimate Costs • Determine Budget		• Control Costs	
Quality Management		• Plan Quality Management	• Manage Quality	• Control Quality	
Resources Management		• Plan Resource Management • Estimate Activity Resources	• Acquire Resources • Develop Team • Manage Team	• Control Resources	
Communication Management		• Plan Communications Management	• Manage Communications	• Monitor Communications	
Risk Management		• Plan Risk Management • Identify Risks • Perform Qualitative Risk Analysis • Perform Quantitative Risk Analysis • Plan Risk Response	• Implement Risk response	• Monitor Risks	
Procurement Management		• Plan Procurement Management	• Conduct Procurement	• Control Procurement	
Stakeholder Management	• Identify Stakeholders	• Plan Stakeholder Engagement	• Manage Stakeholder Engagement	• Monitor Stakeholder Engagement	

✓ CONTROL PROCUREMENT

INPUTS

TECHNIQUES


OUTPUTS

- Project Management Plan
- Project Documents
- Agreements
- Procurement Documentation
- Approved Change Requests
- Work Performance Data
- Enterprise Environmental Factors
- Organizational Process Assets

- Expert Judgement
- Claims Administration
- Data Analysis
- Inspection
- Audits

- Closed Procurement
- Work Performance Information
- Change Requests
- Project Management Plan updates
- Project Document updates
- Organizational Process Assets updates

• LE DATA FLOW PROJECT PROCUREMENT MANAGEMENT

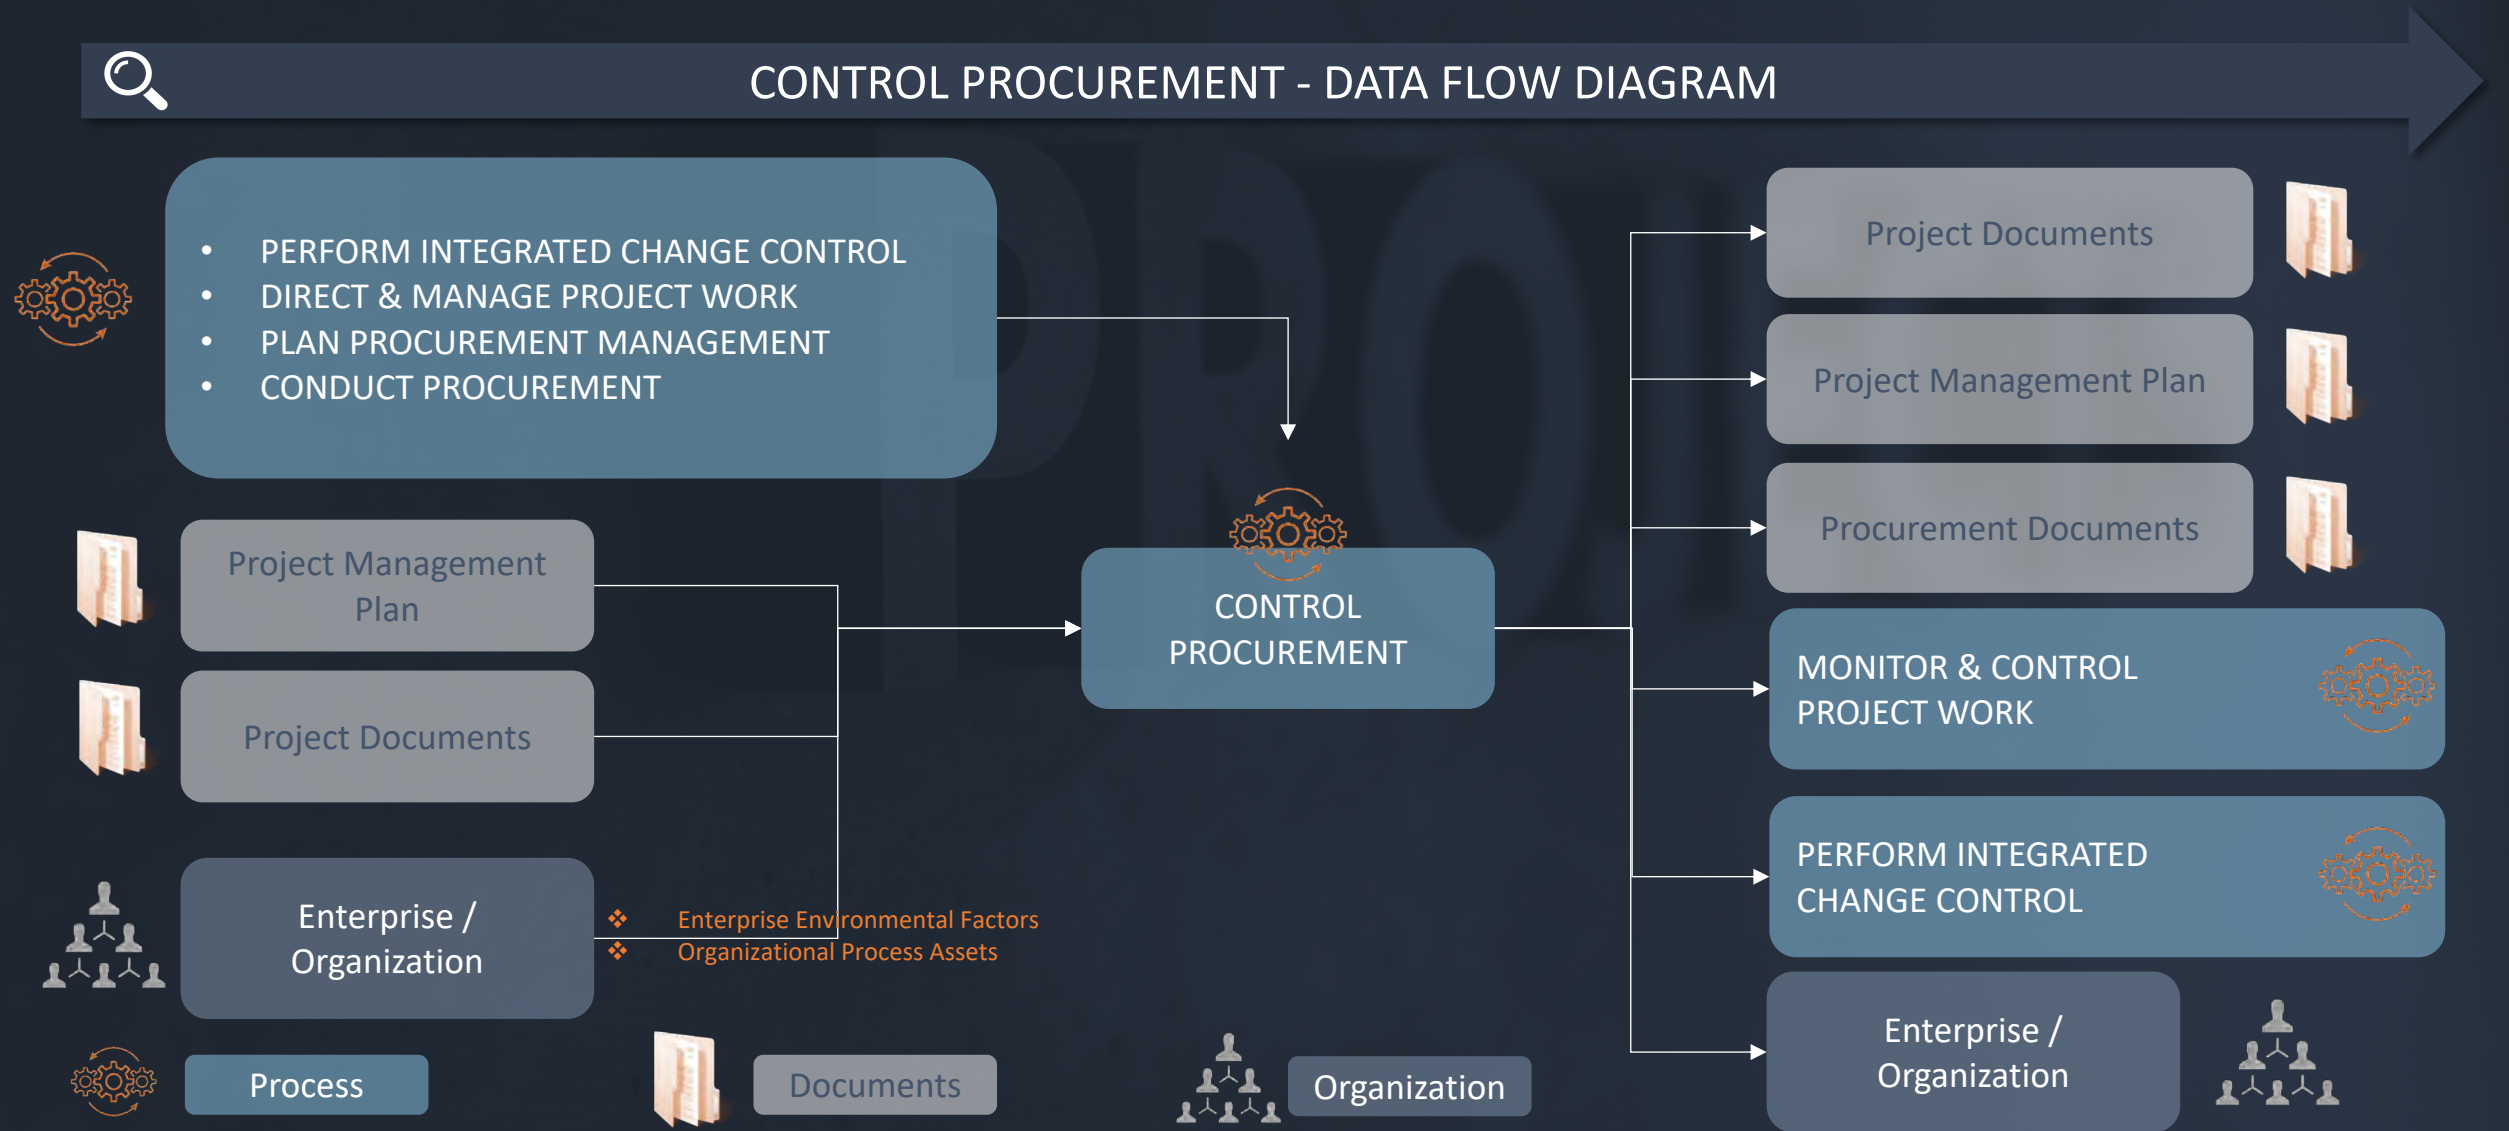

• LES NOTIONS ESSENTIELLES PROJECT PROCUREMENT MANAGEMENT

	Project Management Process Group				
	INITIATING	PLANNING	EXECUTING	MONITORING & CONTROLLING	CLOSING
Integration Management	• Develop Project Charter	• DEVELOP PROJECT MANAGEMENT PLAN	• Direct & Manage Project Work • Manage Project Knowledge	• Monitor & Control Project Work • Perform Integrated Change Control	• Close Project or Phase
Scope Management		• Plan Scope Management • Collect Requirement • Define Scope • Create WBS		• Validate Scope • Control Scope	
Schedule Management		• Plan Schedule Management • Define Activities • Sequence Activities • Estimate Activities • Develop Schedule		• Control Schedule	
Cost Management		• Plan Cost Management • Estimate Costs • Determine Budget		• Control Costs	
Quality Management		• Plan Quality Management	• Manage Quality	• Control Quality	
Resources Management		• Plan Resource Management • Estimate Activity Resources	• Acquire Resources • Develop Team • Manage Team	• Control Resources	
Communication Management		• Plan Communications Management	• Manage Communications	• Monitor Communications	
Risk Management		• Plan Risk Management • Identify Risks • Perform Qualitative Risk Analysis • Perform Quantitative Risk Analysis • Plan Risk Response	• Implement Risk response	• Monitor Risks	
Procurement Management		• Plan Procurement Management	• Conduct Procurement	• Control Procurement	
Stakeholder Management	• Identify Stakeholders	• Plan Stakeholder Engagement	• Manage Stakeholder Engagement	• Monitor Stakeholder Engagement	



- Procurement Processes
- Procurement Strategy
- Contract & Legal dimensions
- Contracts types & Change Contracts
- Bid Documents
- Industrial Organization
- Sourcing Strategy
- Selection & Partnership Strategy
- Earned Value Analysis
- Cost Baseline
- Cost Budget
- Independent Cost estimate
- Waivers & Claims management
- NDA – Non Disclosure Agreement

- LES QUESTIONS PROJECT PROCUREMENT MANAGEMENT

Question

1/ What's the best to do for a PM during Conduct Procurement phase ? :

- A) Evaluate risks
- B) Select a contract type
- C) Market Research
- D) Answer seller's questions

• LES QUESTIONS PROJECT PROCUREMENT MANAGEMENT

Answer

1/ What's the best to do for a PM during Conduct Procurement phase ? :

- A) Evaluate risks
- B) Select a contract type
- C) Market Research
- D) Answer seller's questions

Réponse: D

Durant la phase Conduct Procurement le Chef de Projet doit s'assurer que l'équipe projet apportent des réponses pertinentes aux questions posées par les vendeurs.

- LES QUESTIONS PROJECT PROCUREMENT MANAGEMENT

Question

2/ What is the main benefit to centralize contracts ? :

- A) Increase expertise
- B) Easier access
- C) PM does not need to be involved
- D) Loyalty to the overall project

• LES QUESTIONS PROJECT PROCUREMENT MANAGEMENT

Answer

2/ What is the main benefit to centralize contracts ? :

- A) Increase expertise
- B) Easier access
- C) PM does not need to be involved
- D) Loyalty to the overall project

Réponse: A

La mutualisation de contrat permet d'accéder plus facilement à des experts du procurement (plus les montants et les volumes sont importants plus le procurement met un focus sur le contrat en question).

- LES QUESTIONS PROJECT PROCUREMENT MANAGEMENT

Question

3/ Which type of contract is a concern for a supplier regarding the scope ?

- A) Fixed Price
- B) Cost plus Fixed Price
- C) Time & Material
- D) Purchase Order

• LES QUESTIONS PROJECT PROCUREMENT MANAGEMENT

Answer

3/ Which type of contract is a real concern for a supplier regarding the scope ?

- A) Fixed Price
- B) Cost plus Fixed Price
- C) Time & Material
- D) Purchase Order

Réponse: A

Le contrat fixe est une source de risk pour un vendeur en cas de mauvaise évaluation initiale du périmètre et du besoin.

Project Management



• FORMEZ-VOUS GRATUITEMENT A LA GESTION DE PROJET !

- #01 INTRODUCTION
- #02 LES PRINCIPES FONDAMENTAUX PM
- #03 LES CONNAISSANCES FONDAMENTALES PM
- #04 LA VALEUR & LES PERFORMANCES PM
- #05 LE REFERENTIEL STANDARD PM
- #06 LE PROCESSUS PROJECT INTEGRATION
- #07 LE PROCESSUS PROJECT SCOPE MANAGEMENT
- #08 LE PROCESSUS PROJECT SCHEDULE MANAGEMENT
- #09 LE PROCESSUS PROJECT COST MANAGEMENT
- #10 LE PROCESSUS PROJECT QUALITY MANAGEMENT
- #11 LE PROCESSUS PROJECT RISK MANAGEMENT
- #12 LE PROCESSUS PROJECT STAKEHOLDER MANAGEMENT
- #13 LE PROCESSUS PROJECT RESOURCE MANAGEMENT
- #14 LE PROCESSUS PROJECT COMMUNICATION MANAGEMENT
- #15 LE PROCESSUS PROJECT PROCUREMENT MANAGEMENT
- #16 LE DOMAINE DE LA PERFORMANCE PROJET
- #17 LE PROCESSUS D'ADAPTATION – PROJECT TAILORING
- #18 LES MODÈLES, METHODES & ARTEFACT PROJECT MANAGEMENT
- #19 PREPARATION A L'EXAMEN PMP®



PM

Se connecter

Formez-vous Gratuitement à la Gestion de Projet

Mes formations certifiantes **CPM®** & **PMP®** sont accessibles en illimité et sans engagement.

FORMATION GRATUITE CPM® 20h

FORMATION GRATUITE PMP® 35h

Offrez-vous +20 ans d'Expérience

Afin de compléter votre formation offerte, je vous Coach **Individuellement**, à votre rythme et exclusivement **selon vos besoins**.

Au travers du coaching, je partage avec vous **+ de 20 ans** d'expérience en **Gestion de Projet & Programme** Satellites & Lanceurs Spatiaux.

Sébastien Coffiney
Airbus Transformation Program Leader
Executive MBA SJTU Shanghai
HEC Paris

www.pm-coaching.org

PM

Project Procurement Management

PROJECTS
